


contract		WEEKLY REPORT #01		INVENTIV- ALEM 855_PISO23		
Proyect Name		Pharmanet / I3		Region		South America
Date		27 de julio 2012		País		Argentina
Constructor		Contract		Ciudad		Buenos Aires
Representante Pharmanet		Wanda Dobrzanski		Edificio		Alem Plaza
Categoría del Proyecto		Oficinas Corporativas		TOTAL AREA		720 m ²
1) FOTOS AVANCE DE OBRA_ 22/06 - 26/07						
						
1		2		3		
						
4	5		6	7		
						
8	9	10		11		
						
12	13	14		15		
						
16	17		18			

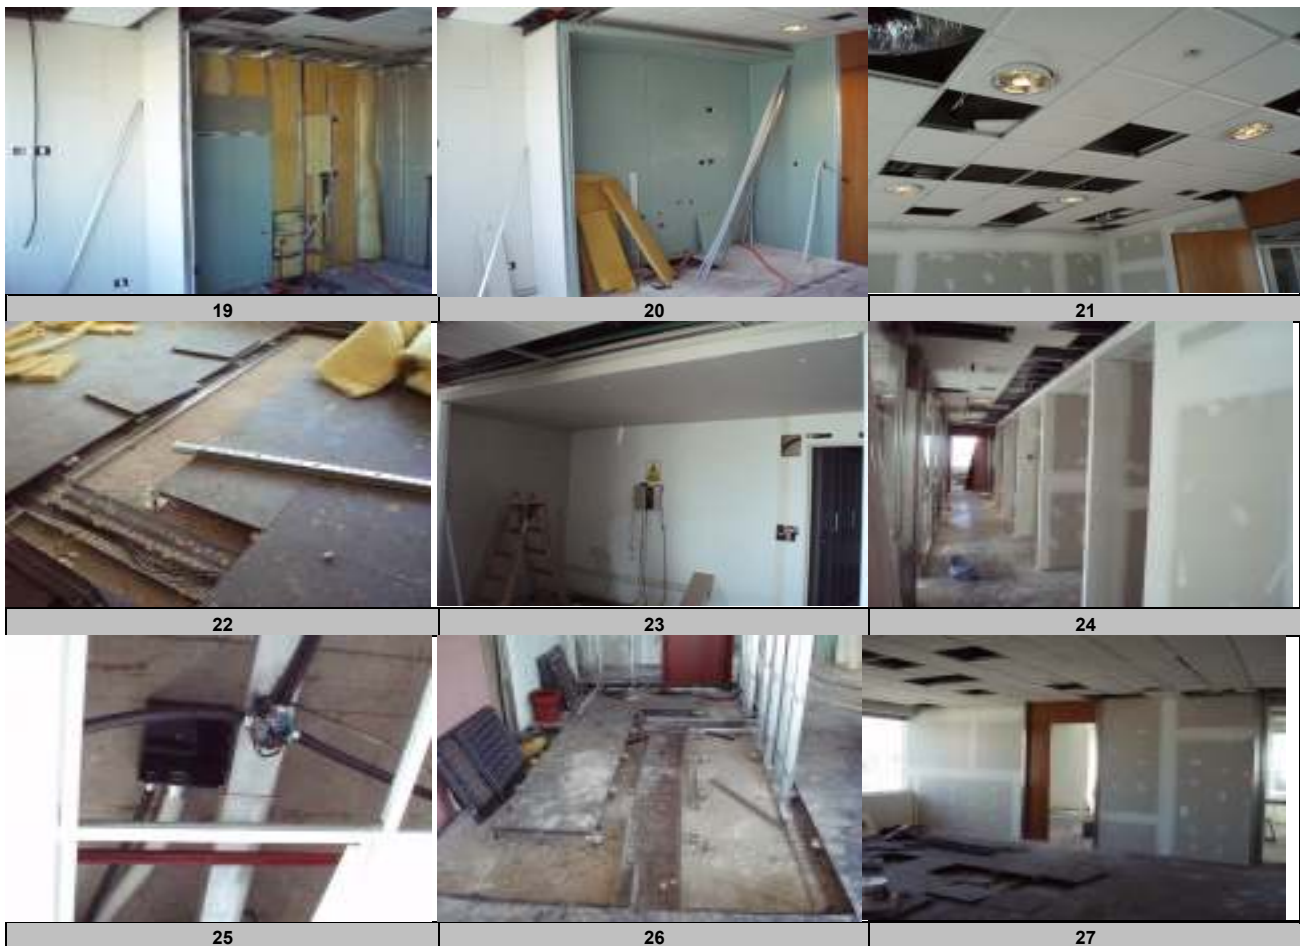

2) TAREAS EJECUTADAS			
Item	Descripción	% Complete	Area
1	Demolitions- removal of carpets.	100%	Open Space
2	Demolitions- removal of carpets and existing partitions	100%	Open Space-boxes
3	Demolitions- removal of carpets and existing bathroom and office	100%	Open Space
4	Interior protections	100%	Elevators hall
5	Demolitions- existing coffee	100%	Director office / coffee
6	Standard bent plate coating (on partitions with existing fabric coverings)	100%	Conference room
7	HVAC- Duct work	100%	General
8	Dry wall partitions - structure and first plate including insulations	100%	Small meeting room
9	Dry wall partitions - structure	100%	Server Room
10	Dry wall partitions - structure	100%	Copy area
11	Ceilings- dry wall structure	100%	Recepcion area
12 & 13	Dry wall partitions - structure and first plate including insulations	100%	Storage room
14	Electrical instalation - conduits	100%	Copy area
15	Fire supresion - piping adaptations Hydrants & Sprinklers	100%	Copy area
16	Adjustment of existing doors & new F60 door for server room.	100%	Coffee(on front) Server R. (back)
17	Plumbing- water & sewage piping cofee/office	100%	Coffee
18	Painting- preparation of walls	5%	General
19 & 20	Dry wall partitions - insulations & second plate	75%	Coffee
21	Electrical instalation - lighting fixtures relocation	15%	Offices
22	Electrical instalation - conduits below raised floor	70%	General
23	Ceilings- dry wall plates	75%	Meeting room (in front moving files room)
24	Dry wall partitions - second plate	75%	corridor
25	Electrical instalation - Conduits above ceiling (audio visual inst.)	100%	Conference room
26	Electrical instalation - conduits below raised floor	70%	Server Room
27	Relocation of existing doors.	100%	Corner office
END OF DOCUMENT			
