




Id		Task Name	Duración	Comienzo	Fin	jun '08	08 jun '08	15 jun '08	22 jun '08	29 jun '08	06 jul '08	13 jul '08	20 jul '08	27 jul '08	03 ago '08	10 ago '08	17 ago '08	24 ago '08	31 ago '0
																			M
76		Colocación de alfombra	1 día	dom 10/08/08	lun 11/08/08														
77		Armado de equipamiento	1 día	dom 10/08/08	lun 11/08/08														
78		Retoques	4 días	lun 11/08/08	vie 15/08/08														
79		Etapla 8	7 días	vie 15/08/08	vie 22/08/08														
80		Desarme de equipamiento	1 día	vie 15/08/08	sáb 16/08/08														
81		Desmonte de alfombra	1 día	vie 15/08/08	sáb 16/08/08														
82		Desmonte de tabiques	1 día	sáb 16/08/08	dom 17/08/08														
83		Armado de tabiques	2 días	vie 15/08/08	dom 17/08/08														
84		Corrimiento de periscopios y puestos nuevos	2 días	vie 15/08/08	dom 17/08/08														
85		Pintura	3 días	vie 15/08/08	lun 18/08/08														
86		Colocación de alfombra	1 día	dom 17/08/08	lun 18/08/08														
87		Armado de equipamiento	1 día	dom 17/08/08	lun 18/08/08														
88		Retoques	4 días	lun 18/08/08	vie 22/08/08														
89		Etapla 9	9 días	vie 22/08/08	dom 31/08/08														
90		Desarme de equipamiento	1 día	vie 22/08/08	sáb 23/08/08														
91		Pulido	1 día	vie 22/08/08	sáb 23/08/08														
92		Armado de equipamiento	1 día	sáb 23/08/08	dom 24/08/08														
93		Terminaciones	7 días	dom 24/08/08	dom 31/08/08														

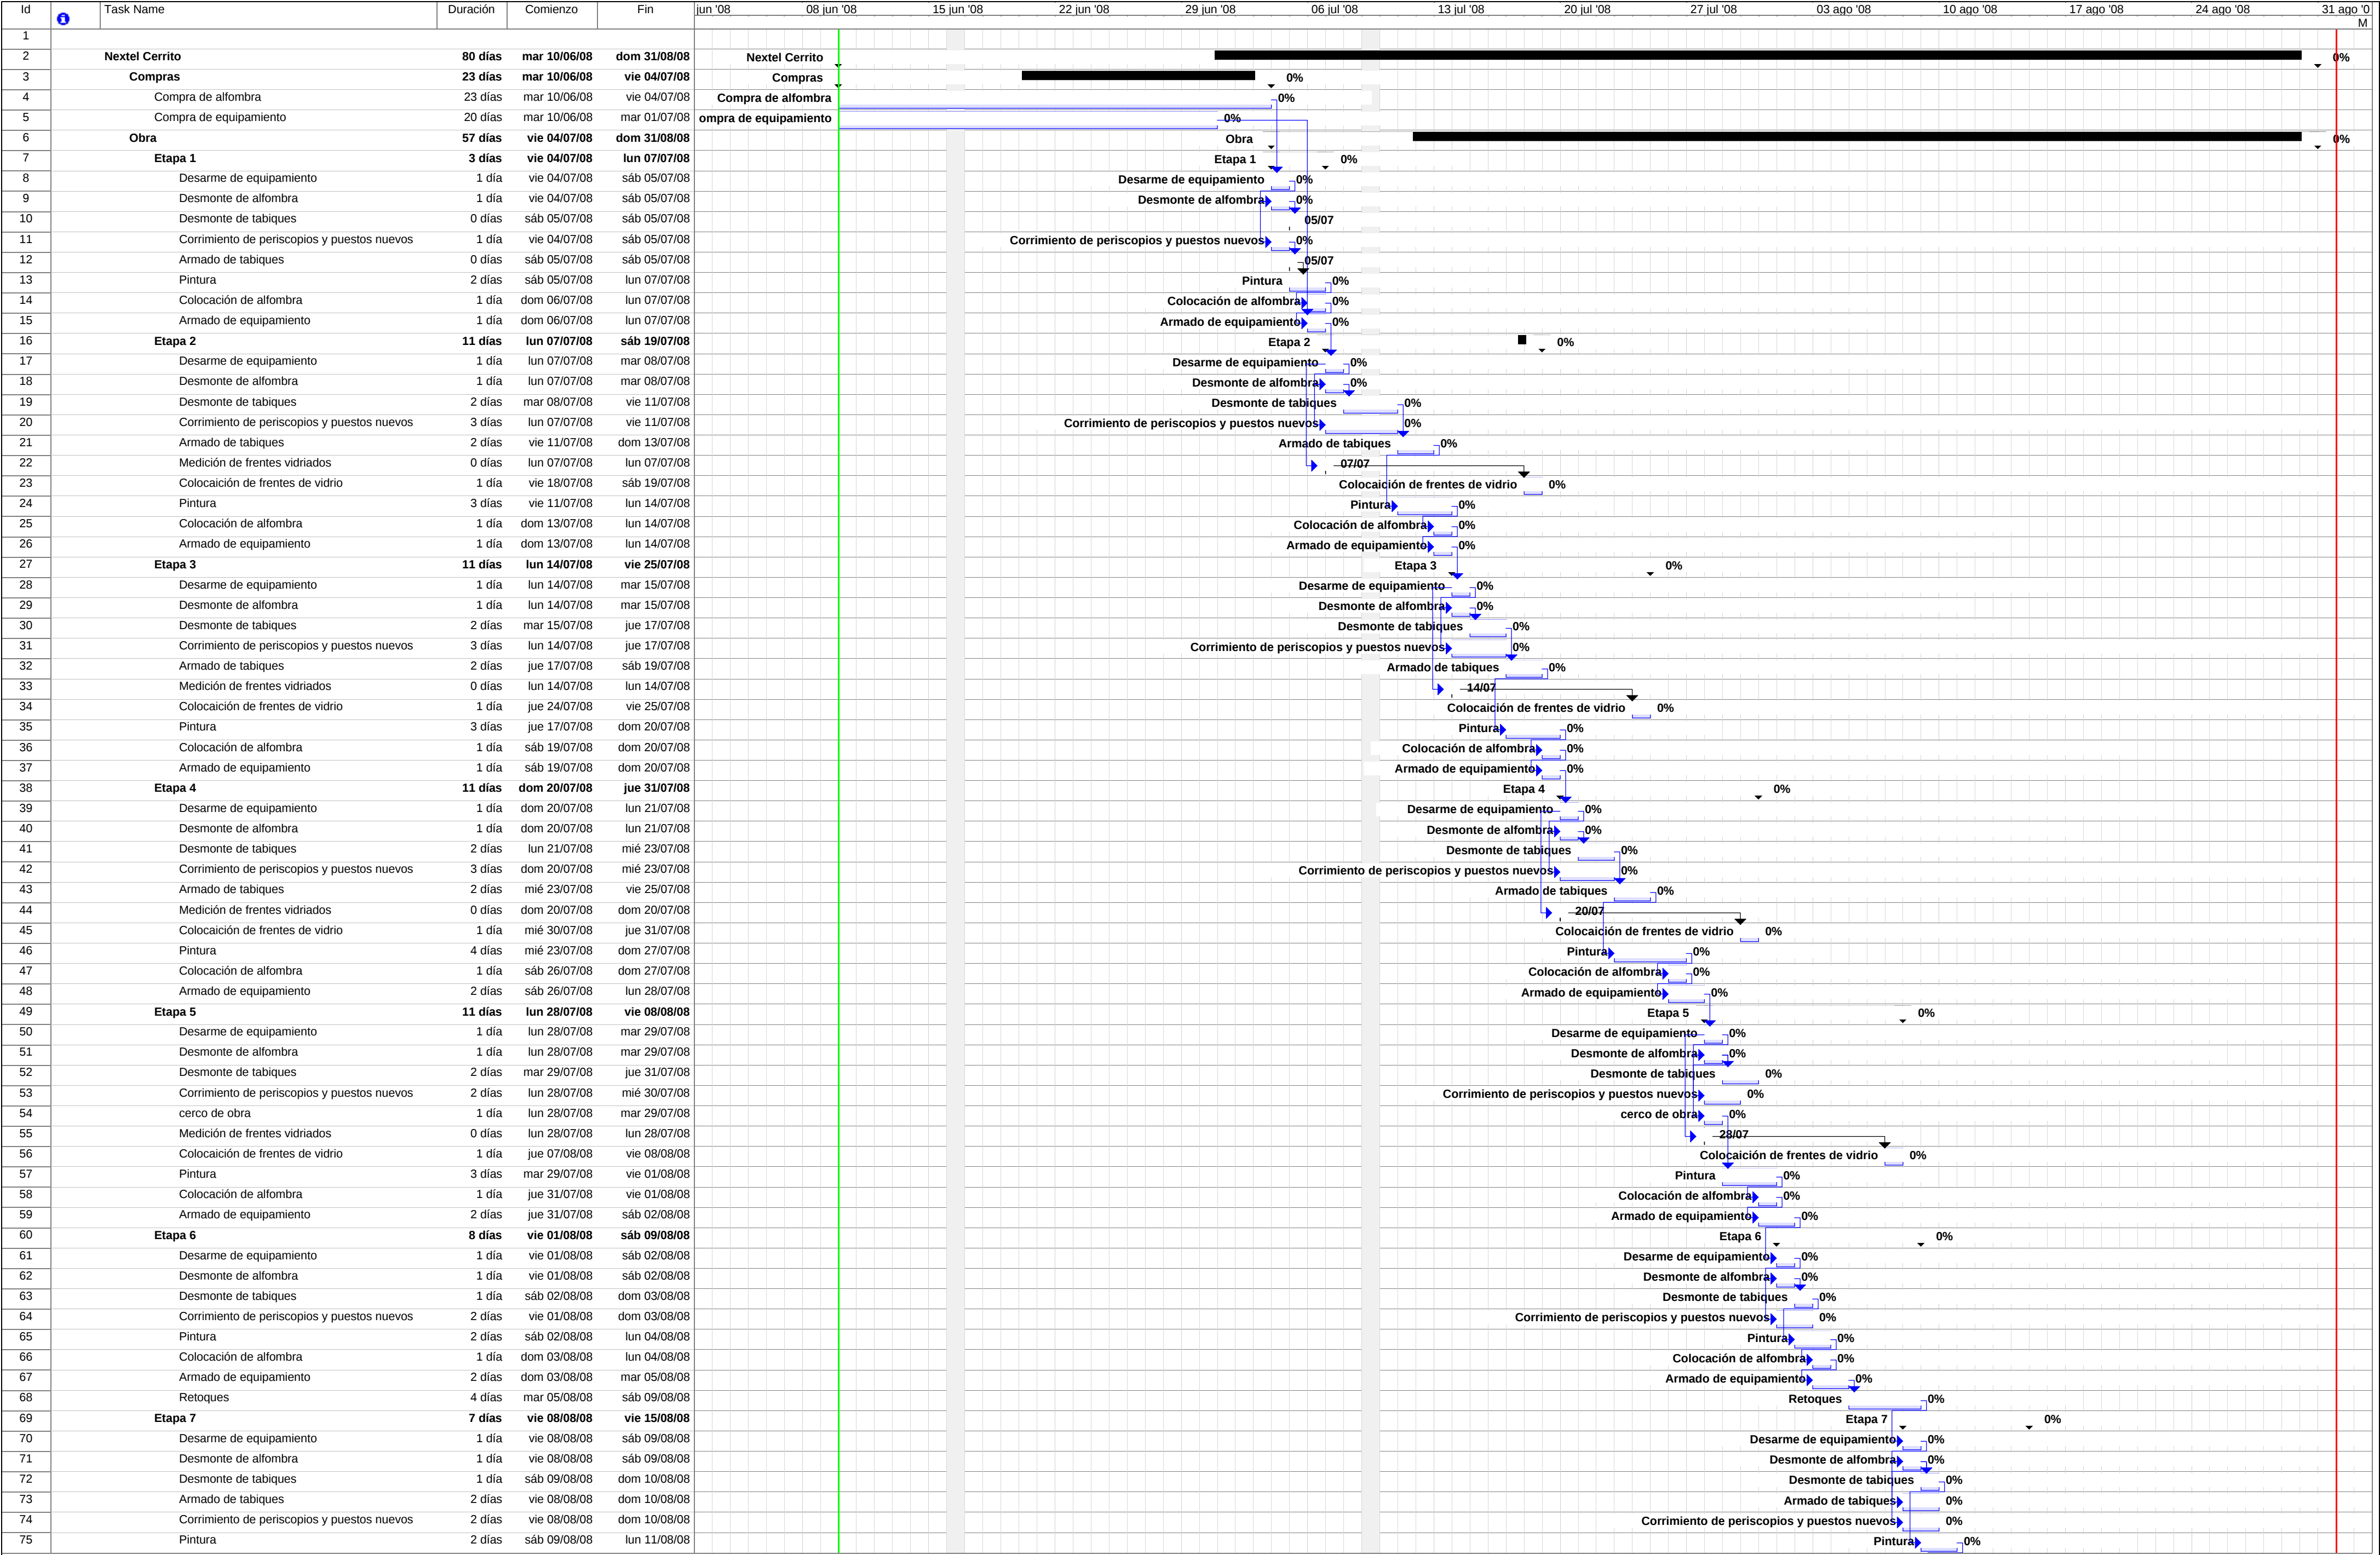
